


# Citrus Community College

Citizens Bond Oversight Committee

Measure G

Bond Program Overview

March 5, 2015



# ***BOND PROJECTS***




# **FINE ARTS BUILDING CONSTRUCTION PROGRESS**

- Total budget of \$20 million
- Construction is moving swiftly
- Major earthwork and underground utilities complete
- Footings and grade beams are in place
- Structural steel 95% complete
- Scheduled completion...August 2016

# FINE ARTS BUILDING





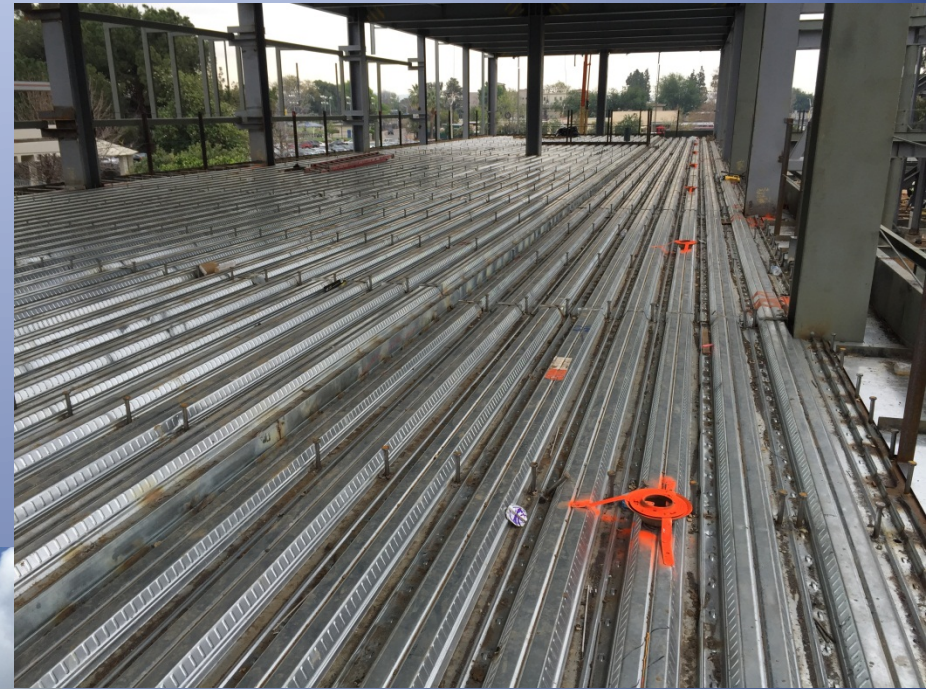





# HAYDEN HALL MODERNIZATION

- Department of Finance has approved funding
- Preliminary plans due by June, 2015
- Westberg + White Architects is the design firm
- Estimated budget of \$4 million
  - 50% Bond-funded
  - 50% State-funded
- DSA submission will commence in summer of 2015
- Construction is estimated to last 1 year





# CAMPUS CENTER MODERNIZATION

- Campus Center...schematic design complete
- Project encompasses upper floor space including space planning, mechanical, electrical and technology systems
- Estimated budget of \$3.7 million
- Planning will begin in Fall of 2015
- Construction scheduled for Summer of 2016
- Construction duration- approximately 1 year
- Initial Project Proposal submitted to the State for possible funding consideration for the food services area





# ED MODERNIZATION

- Preliminary planning is in progress
- Ziemba + Prieto Architects re-established as built conditions
- Last bond project to be completed due to use of facility for swing space
- Estimated budget of \$3.5 million
- Planning phase to begin in Fall of 2016
- Construction scheduled to begin Spring of 2018
- Estimated 1 year construction project



# Questions...

