

Citrus Community College

Citizens Bond Oversight Committee

Measure G


Bond Program Overview

March 24, 2016



FINE ARTS BUILDING CONSTRUCTION PROGRESS


- Total budget of \$20 million
- Scheduled completion...August 2016
- Construction continues to move swiftly and is **AHEAD** of schedule...
- All major building systems are in place
- Interior finish products and equipment are in process
- Exterior finish flatwork and landscaping are in process
- Punch list is forthcoming quickly



FINE ARTS BUILDING





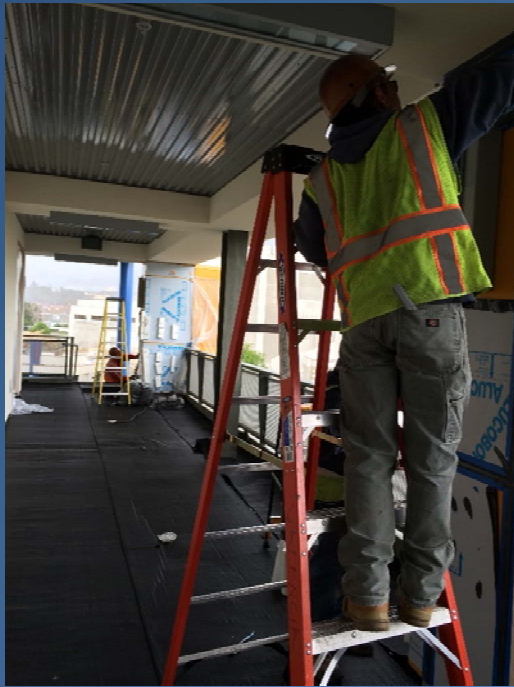

HAYDEN HALL MODERNIZATION

- Westberg + White Architects is the design firm
- Estimated budget of \$4 million
 - 50% Bond-funded
 - 50% State-funded
- DSA has finished review and the plans are APPROVED
- Chancellor's Office and DOF are finishing their review now
- Bidding phase will commence very soon
- Construction is estimated to last 1 year



CAMPUS CENTER MODERNIZATION

- Campus Center...schematic design complete
- Project encompasses upper floor space including space planning, mechanical, electrical and technology systems
- Estimated budget of \$4 million
- Design documents are underway
- Construction bidding is calendared for Summer of 2016
- Construction duration-approximately 1 year
- Initial Project Proposal submitted to the State for possible funding consideration for the food services area—project funding was denied



ED MODERNIZATION

- Westberg + White Architects is the design team
- Preliminary planning is in progress
- Last bond project to be completed due to use of facility for swing space
- Estimated budget of \$3.5 million
- Planning phase to begin in Fall of 2016
- Construction scheduled to begin in Spring of 2018
- Construction time is 1 year



Questions...

