


Citrus Community College

Citizens Bond Oversight Committee

Measure G

Bond Program Overview

September 24, 2015



BOND PROJECTS




FINE ARTS BUILDING CONSTRUCTION PROGRESS

- Total budget of \$20 million
- Construction continues to move swiftly and is on schedule
- All utilities are installed
- All wall systems and facades are in place and are receiving finishes
- Interior built-ins are in process
- Scheduled completion...August 2016

FINE ARTS BUILDING





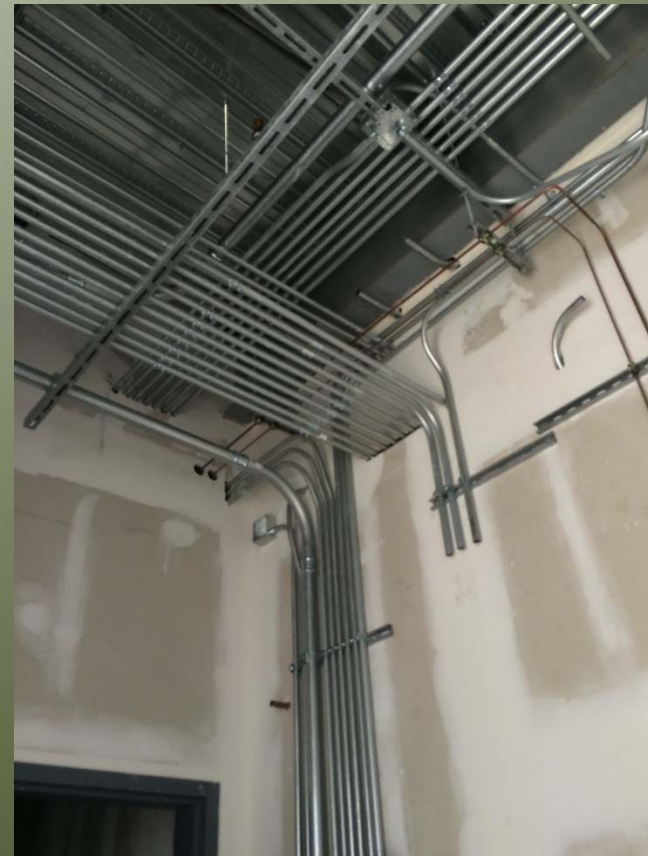

HAYDEN HALL MODERNIZATION

- Estimated budget of \$4 million
- Westberg + White Architects is the design firm
 - 50% Bond-funded
 - 50% State-funded
- DSA plan submission was done in August, 2015
- Bidding will likely commence in late 2015 with a bid award in January, 2016
- Construction is estimated to last 1 year



CAMPUS CENTER MODERNIZATION

- Campus Center...schematic design complete
- Project encompasses upper floor space including space planning, mechanical, electrical and technology systems
- Estimated budget of \$3.7 million
- Design programming is underway
- Construction is calendared for Summer of 2016
- Construction duration-approximately 1 year
- Initial Project Proposal submitted to the State for possible funding consideration for the food services area—as a separate project



ED MODERNIZATION

- Preliminary planning is in progress
- Ziemba + Prieto Architects re-established as built conditions
- Last Measure G project to be scheduled due to use of facility for swing space needs
- Estimated budget of \$3.5 million
- Planning phase to begin in Fall of 2016
- Construction scheduled to begin Spring of 2018
- Estimated 1 year construction project



Questions...

