

Citrus Community College

Citizens Bond Oversight Committee

Measure G

Bond Program Overview

December 13, 2018



CAMPUS CENTER MODERNIZATION



CAMPUS CENTER MODERNIZATION

- Project encompasses upper floor space planning, mechanical, electrical and technology systems
- Westberg + White Architects is the design team
- Horizons Construction is the general contractor
- Bid award was for \$3,647,000
- Notice to Proceed issued October 9, 2017
- Construction duration is approximately 1 year



CAMPUS CENTER MODERNIZATION

- Project is 95% complete
- Finish painting underway
- Finish electrical underway
- Finish equipment underway
- Finish flooring underway
- Major electrical scheduled for winter break



CAMPUS CENTER MODERNIZATION



- Equipment
- Flooring
- Casework
- Finishes

CAMPUS CENTER MODERNIZATION




- Flooring
- Acoustics
- Lighting
- Finishes

CAMPUS CENTER MODERNIZATION

- Offices
- Meeting Space



CAMPUS CENTER MODERNIZATION

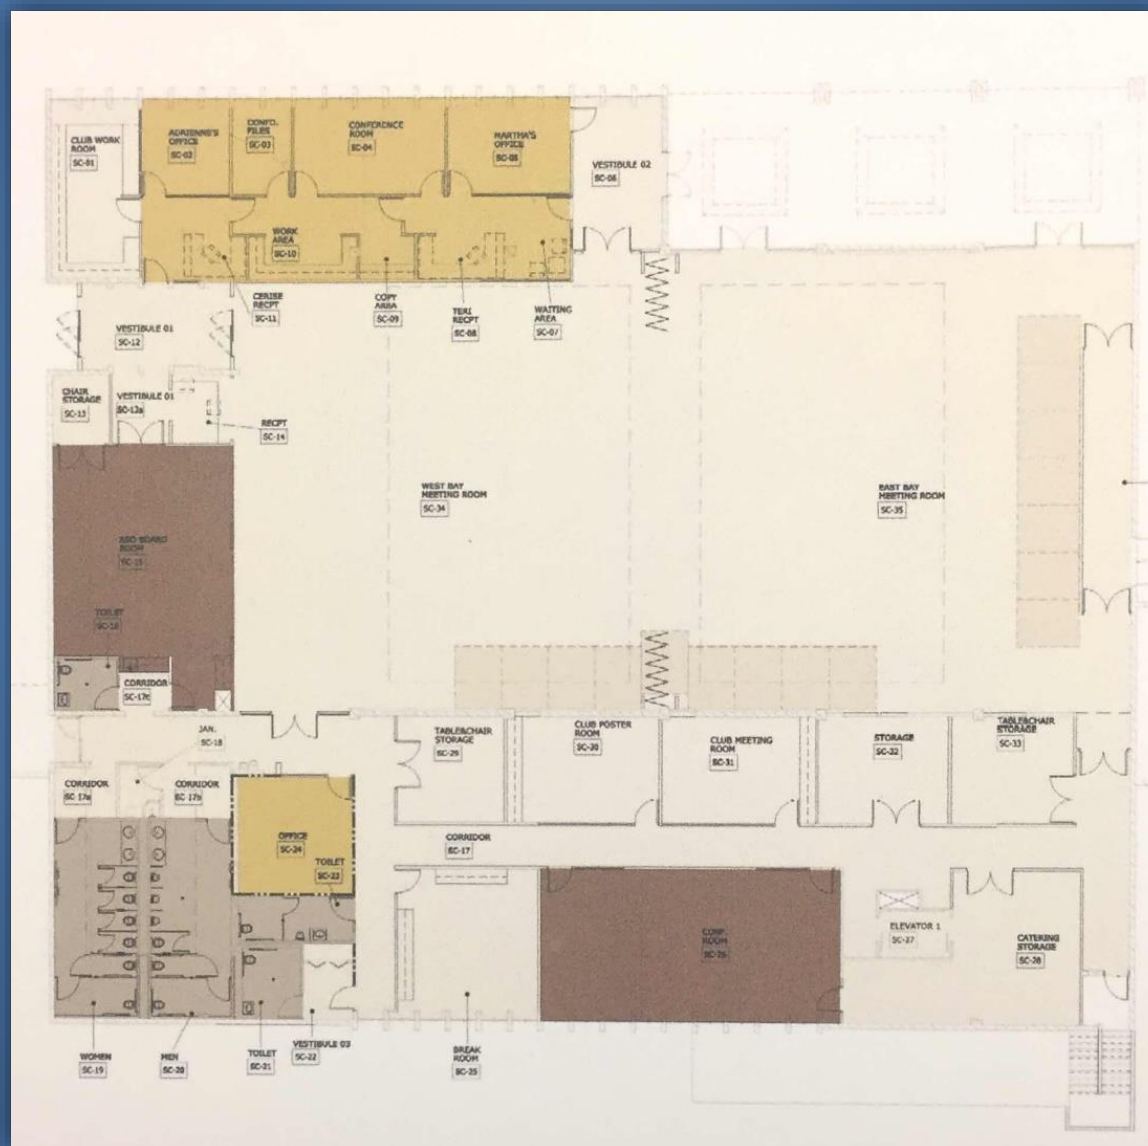

FOOTBALL PRACTICE FIELD

- Capital Outlay
- \$492,000
- KYA Group
- FCCC Contract
- Completed in one month



FOOTBALL PRACTICE FIELD



ED MODERNIZATION

- Westberg + White Architects
- Schematic drawings complete
- 2nd stakeholder meeting in process
- ED is the last bond project to be completed due to use of facility as swing space
- Building will be returned to classroom & laboratory space
- \$3.5 million original bond budget
- Construction will begin upon Campus Center completion, DSA approval and bidding
- Construction duration is 1 year



Questions...

