

Citrus Community College

Citizens Bond Oversight Committee

Measure G

Bond Program Overview

December 14, 2017



CAMPUS CENTER MODERNIZATION



CAMPUS CENTER MODERNIZATION

- Project encompasses upper floor space planning, mechanical, electrical and technology systems
- Westberg + White Architects is the design team
- Horizons Construction is the general contractor
- Bid award was for \$3,647,000
- Notice to Proceed issued October 9, 2017
- Construction duration is approximately 1 year



CAMPUS CENTER MODERNIZATION



Demolition
Underway



CAMPUS CENTER MODERNIZATION



CAMPUS CENTER MODERNIZATION




TD ENGINE DYNAMOMETERS

- Aire-Masters is the Contractor
- Project Budget is \$1.1 million
- Award of contract for \$992,468
- Notice to Proceed: December 6, 2016
- Construction duration: 6 months
- Commissioning is underway



TD ENGINE DYNAMOMETERS

- Engine Testing & Calibration
- Sound Attenuation

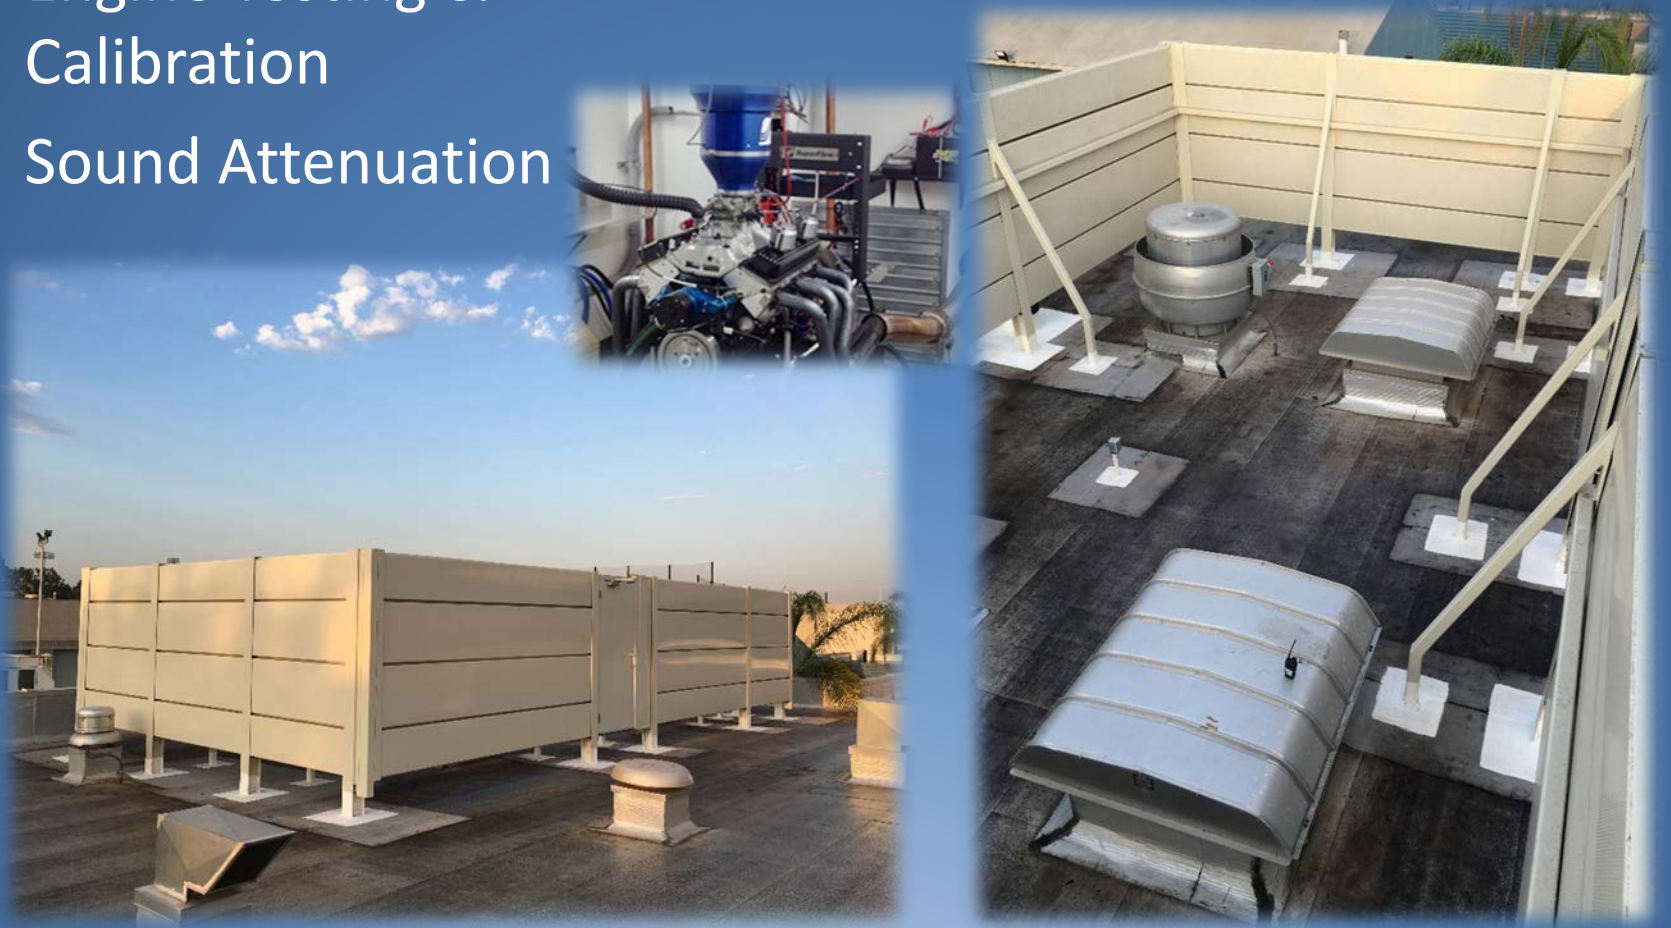

TD ENGINE DYNAMOMETERS

- Pump Systems
- Control Systems



ED MODERNIZATION

- Westberg + White Architects
- Preliminary planning is in progress
- ED is the last bond project to be completed due to use of facility as swing space
- Building will be returned to classroom & laboratory space
- \$3.5 million original bond budget
- Planning phase has begun
- Construction will begin upon Campus Center completion
- Construction duration is 1 year



Questions...

